

AGENDA

COMMITTEE ON JOINT SCHOOL BUILDINGS

February 6, 2007

**School Cmte. Members Beaudry,
Herbert, Gelinas
Aldermen Thibault, Roy, Long**

5:00 PM

**Aldermanic Chambers
City Hall (3rd Floor)**

1. Chairman Beaudry calls the meeting to order.
2. The Clerk calls the roll.
3. Update on the School Facilities Improvement Project (Monthly Report – February 2007).
A motion would be in order to accept the report and forward it to the Board of Mayor and Aldermen for informational purposes.
4. Communication from the Building & Sites Committee requesting if the cost for the roof structure repairs at Hallsville School could come from the contingency fund of the design/build project.
Gentlemen, what is your pleasure?
5. If there is no further business, a motion is in order to adjourn.



Monthly Report – February 2007

City of Manchester
Joint School Building Committee Meeting: February 6, 2007
School Facilities Improvement Project

1.0 Budget:

- Budget overview summary attached

2.0 Schedule:

- Project schedule overview attached.

Activity Summary:

Construction activity continues to be executed primarily on night-shift hours, with the exception of December school vacation week (day shift). Central High School, Memorial High School classroom addition, Southside Middle School and Hillside Middle School classroom additions are all in full use by students and faculty and continue to have ongoing punchlist activities. Most schools have undergone a majority of the punchlist process with miscellaneous isolated interior spaces and exterior (roof, exterior, etc.) remaining. Contractors continue to work on addressing and closing out miscellaneous punchlist items. The Design-Builder and associated contractors also continue to work on more global Program-Wide items such as HVAC system noise mitigation issues (including sound attenuation installation and duct reconfiguration) and door hardware issues.

3.0 Previous Months' Progress (21 December 06 – 01 February 07):

High Schools

- West High School
 - MEP Work Nearly Complete
 - Sound Attenuation Complete (Testing Pending)
 - Punchlist
- Memorial High School
 - Interior Renovation MEP Nearly Complete
 - Sound Attenuation Installation Ongoing
 - Ceiling Tile Replacement Ongoing
 - Punchlist
- Central High School
 - Sound Attenuation Installation Ongoing
 - Punchlist

Middle Schools

- Hillside Middle School
 - Final MEP Nearly Complete
 - Sound Attenuation Nearly Complete
 - Ceiling Tile Replacement Ongoing
 - Punchlist
- Southside Middle School
 - Final MEP Nearly Complete
 - Ceiling Tile Replacement Ongoing
 - Sound Attenuation Installation Ongoing
 - Punchlist
- Parkside Middle School



- Punchlist

Elementary Schools

- Wilson Elementary School
 - Exterior Door Installation Complete
 - Punchlist
- Beech Street Elementary School
 - MEP Installation Nearly Complete
 - Punchlist
- Hallsville
 - Door Installation Nearly Complete
 - Punchlist
- Bakersville Elementary School
 - Sound Attenuation Complete (Testing Pending)
 - Door Replacement Complete
 - Punchlist
- McDonough Elementary School
 - Sound Attenuation Installation
 - Punchlist
- Gossler Park Elementary School, Jewett Street Elementary School, Smyth Road Elementary School, Webster Elementary School, Parker Varney Elementary School, Weston Elementary School, Highland Goffs Falls Elementary School and Green Acres Elementary School
 - Punchlist
- Ongoing Weekly Project Status Meetings

4.0 Upcoming Activities (02 February 07 – 28 February 07):

High Schools

- West High School
 - MEP Work Completion
 - Punchlist
- Memorial High School
 - MEP Interior Renovations Continues
 - Sound Attenuation Installation Continues
 - Punchlist
- Central High School
 - Punchlist

Middle Schools

- Hillside Middle School
 - Final MEP Nearing Completion
 - Sound Attenuation Installation Nearing Completion
 - Punchlist
- Southside Middle School
 - Final MEP Nearing Completion
 - Sound Attenuation Installation Continues
 - Roof Duct Tie-down Work Continues
 - Punchlist
- Parkside Middle School
 - Punchlist



Elementary Schools

- Wilson Elementary School
 - Exterior Door Installation Completion
 - Punchlist
- Beech Street Elementary School
 - Punchlist
- Hallsville
 - Door Installation Nearing Completion
 - Punchlist
- Bakersville Elementary School, Gossler Park Elementary School, Jewett Street Elementary School, Smyth Road Elementary School, Webster Elementary School, McDonough Elementary School, Parker Varney Elementary School, Weston Elementary School, Highland Goffs Falls Elementary School and Green Acres Elementary School
 - Punchlist

5.0 Critical Issues:

- Punchlisting
- Sound Attenuation Work
- Door Hardware Work

6.0 New Issues:




7.0 Progress Photos

Late December to Early February

McDonough Sound Attenuation Work – Additional Diffuser



Southside Middle School Abandoned FA System Removal

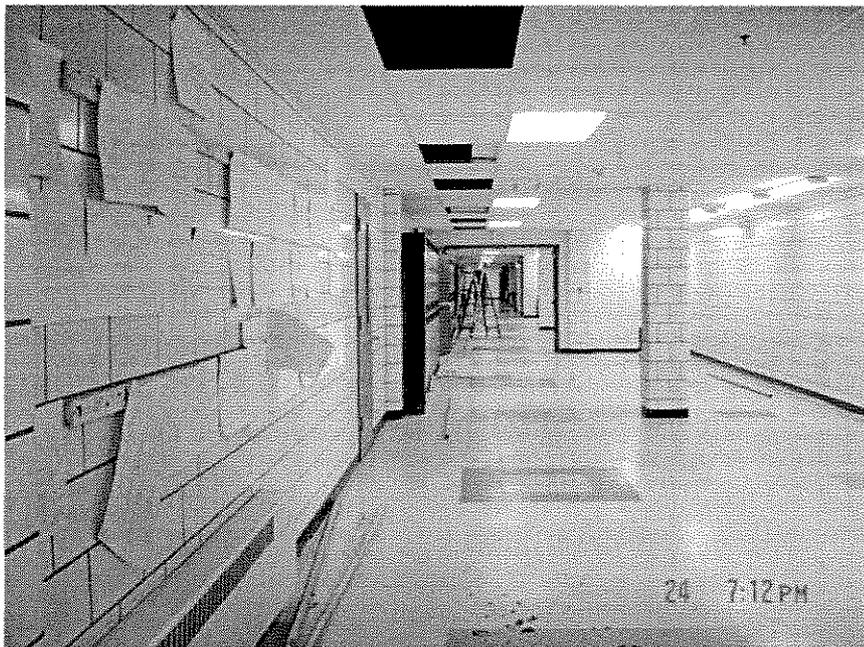

3



JOINT SCHOOL BUILDING COMMITTEE

HIGHWAY DEPARTMENT / PROJECT FINANCIAL REPORT

1-Feb-07

DESIGN/BUILD/FINANCE SCHOOL IMPROVEMENT PROGRAM - Project #310303

BUDGET	FUNDING	SOURCE:	Bond
		FY03 CIP	School Revenue Bond
	FY03 CIP	Gen.Obligation Bond	\$3,590,000
	FY03 CIP	Earned Interest	\$3,995,000
109,247,719	FY05	School Admin.Funding	\$252,719

AUTHORIZED VENDOR DESCRIPTION AND APPROVAL DATE	BUDGET	AMOUNT ENCUMBERED	PERCENT COMPLETE	AMOUNT EXPENDED	RETAINAGE HELD
INSURANCE & LEGAL					
Arthur J. Gallagher & Co.					
Insurance Administrative & Broker Services	\$250,000.00	\$0.00	100%	\$250,000.00	
Primary Insurance of \$25,000,000	\$265,000.00	\$0.00	100%	\$265,000.00	
Excess Insurance of \$25,000,000	\$130,000.00	\$0.00	100%	\$130,000.00	
Liberty Mutual Insurance Company					
OCIP Premiums	\$1,479,523.00	\$0.00	100%	\$1,479,523.00	
Workmen's Compensation Premium	\$25,000.00	\$0.00	100%	\$25,000.00	
OCIP Loss Fund	\$447,981.61		100%	\$447,981.61	
Insurance Reserve - Future Wk.Comp & Gen.Liabil.Claims	\$223,824.47	Contingency??	0%		
Fernando Insurance - CHS Statue Insure	\$7,500.00	\$0.00	100%	\$7,500.00	
Fernando Insurance - Builders Risk Insurance	\$26,080.00	\$0.00	100%	\$26,080.00	
Ropes & Gray - Consultant Services	\$138,321.64	\$0.00	100%	\$138,321.64	
Albert Risk Management Consultants - OCIP	\$2,217.75	\$0.00	100%	\$2,217.75	
Insurance & Legal To Date	\$2,995,448.47				
PROGRAM MANAGEMENT					
Program Management Services					
DMJM H&N (See contingency for contract amendment)	\$3,141,000.00	\$0.00	100%	\$3,141,000.00	
OTHER EXPENSES					
Information Systems - Computer equipment & Remote Ser	\$1,009.95	\$0.00	100%	\$1,009.95	
PSNH - West HS 3Phase High Voltage Install	\$5,000.00	\$0.00	100%	\$5,000.00	
PSNH - Central HS 3Phase Primary & Transformer	\$15,205.99	\$0.00	100%	\$15,205.99	
Seacoast Diversified - West HS Strip lead paint	\$4,920.00	\$0.00	100%	\$4,920.00	
CED TwinState - Smyth,Jewet,Gossler Light Fixtures	\$2,815.57	\$0.00	100%	\$2,815.57	
Building Permits	\$753,187.65	\$0.00	100%	\$753,187.65	
United Oil Recovery -Remove oil from CHS tank	\$2,761.25	\$0.00	100%	\$2,761.25	
RPF Associates, Inc. - Dust Settling Testing	\$1,772.50	\$0.00	100%	\$1,772.50	
RPF Associates, Inc. - Lead Paint Testing	\$1,156.24	\$0.00	100%	\$1,156.24	
Alpha Asbestos - Lead Paint Removal West HS Railings	\$2,450.00	\$0.00	100%	\$2,450.00	
Alarmax - Smoke Detectors for Webster	\$669.29	\$0.00	100%	\$669.29	
Highway Dept. - Pavement Patching @ Webster	\$1,975.46	\$0.00	100%	\$1,975.46	
WW Grainger - Portable Blowers for Hillside/Southside She	\$809.56	\$0.00	100%	\$809.56	
Century Mechanical - Southside Shelter Exhaust Fans	\$894.31	\$0.00	100%	\$894.31	
Foley & Buhl Engineering - Hallsville Assessment	\$3,800.00	\$0.00	100%	\$3,800.00	
Damon Insulation Co. - insulate Rain Leader Southside	\$1,950.00	\$0.00	100%	\$1,950.00	
Alpha Asbestos - Hang Plastic Southside Shelter	\$1,475.00	\$0.00	100%	\$1,475.00	
RPF Associates - Memorial Asbestos Sampling	\$496.00	\$0.00	100%	\$496.00	
RPF Associates - Beech Dust Settling testing	\$3,349.00	\$0.00	100%	\$3,349.00	
Scott Lawson - Beech St. Abatement Consultant	\$1,660.25	\$0.00	100%	\$1,660.25	
Alpha Asbestos - Classical ACM Floor Core samples	\$2,175.00	\$0.00	100%	\$2,175.00	
Wood Science Specialists - CHS-C Flooring	\$1,917.30	\$0.00	100%	\$1,917.30	
Pelmac Industries - Southside move intercom @ front door	\$560.00	\$560.00	0%		
Other Expenses To Date	\$812,010.32				

3



DESIGN BUILD PROJECT - PAGE 3 OF 5

AUTHORIZED VENDOR DESCRIPTION AND APPROVAL DATE	BUDGET	AMOUNT ENCUMBERED	PERCENT COMPLETE	AMOUNT EXPENDED	RETAINAGE HELD
(Program FF&E-continued)					
Telephone Technologies- CHS/Hillside/Gr.Acres Portable C	\$3,020.00	\$0.00	100%	\$3,020.00	
Interstate Electric - CHS Portable Disconnect FA	\$518.00	\$0.00	100%	\$518.00	
BK Systems - Gr.Acres/Hillside Disconnect FA	\$1,859.00	\$0.00	100%	\$1,859.00	
GA Lafamme -Gr.Acres Power Portable/Wire FA System	\$11,212.89	\$0.00	100%	\$11,212.89	
Mr. Fix-It - Gr.Acres & Hillside Portable Ramps	\$4,990.00	\$0.00	100%	\$4,990.00	
Paul Cloutier - Gr.Acres/Hillside Portable Sitework	\$12,730.00	\$0.00	100%	\$12,730.00	
Century Mechanical - Gr.Acres Portable Plumbing Install	\$7,225.00	\$0.00	100%	\$7,225.00	
Information Systems - Printer ,Server & Software	\$20,290.74	\$0.00	100%	\$20,290.74	
Hillyard - Central Safety Cabinets	\$5,025.00	\$0.00	100%	\$5,025.00	
School District - Reimburse Central HS Appliances	\$3,873.91	\$0.00	100%	\$3,873.91	
Pelmac-Gossler Intercom/MHS & Southside Port. Disconnect	\$462.50	\$0.00	100%	\$462.50	
Perkins - Central HS Sterilizer	\$7,609.00	\$0.00	100%	\$7,609.00	
Wards Natural Science -CHS,Southside,Hillside Science E	\$68,017.05	\$0.00	100%	\$68,017.05	
Conway Office - Six Copiers	\$83,995.00	\$0.00	100%	\$83,995.00	
Barnstead International - Central HS Distillers	\$9,965.84	\$0.00	100%	\$9,965.84	
Alert Scientific Inc - Central Distiller Installation	\$1,325.00	\$0.00	100%	\$1,325.00	
Decker Inc. - School Floor Savers	\$39,705.02	\$0.00	100%	\$39,705.02	
Delta Education - Central Science Equipment	\$320.38	\$0.00	100%	\$320.38	
Educational Innovations - Central Science Equipment	\$119.19	\$0.00	100%	\$119.19	
Frey Scientific - Hillside & Southside Science Equipment	\$3,490.56	\$0.00	100%	\$3,490.56	
J.Sailese & Sons - Memorial Locker Repairs	\$13,420.00	\$0.00	100%	\$13,420.00	
Nasco - Memorial Art Tables	\$4,744.00	\$0.00	100%	\$4,744.00	
Pasco - Central Science Equipment	\$6,594.27	\$0.00	100%	\$6,594.27	
Sargent-Welch - CHS, MHS & Southside Science Equip.	\$36,881.26	\$0.00	100%	\$36,881.26	
Sargent-Weich - CHS & MHS Credit for returned goods	(\$5,429.66)	\$0.00	100%	(\$5,429.66)	
Schiavi-Portable Move Hillside,Gr.Acres,Southside&MHS	\$39,354.97	\$0.00	100%	\$39,354.97	
SK Boreal Lab - Central & Southside Science Equipment	\$4,306.59	\$0.00	100%	\$4,306.59	
OfficeMax - Hillside & Southside Projectors	\$1,598.00	\$0.00	100%	\$1,598.00	
Tice Associates - Southside Microscopes	\$9,900.00	\$0.00	100%	\$9,900.00	
Vernier Software & Tech. - Central Science Equipment	\$11,598.23	\$0.00	100%	\$11,598.23	
School Furnishings - McDonough Cafeteria Tables	\$29,100.60	\$0.00	100%	\$29,100.60	
JR Pepper Electric - Reinstall Light Poles MHS Rear	\$7,472.00	\$0.00	100%	\$7,472.00	
Highway-Southside Extend Pkg.Lot&Curb&Remove Decks	\$6,793.67	\$0.00	100%	\$6,793.67	
Home Depot - 4" Lever caps for Portable capoffs	\$15.92	\$0.00	100%	\$15.92	
Evans Line Constructio - Southside Remove transformers	\$2,000.00	\$0.00	100%	\$2,000.00	
Bio-Rad Laboratories - MHS Electrophoresis Station	\$2,371.27	\$0.00	100%	\$2,371.27	
Carolina Biology - MHS Science Equipment	\$5,631.68	\$0.00	100%	\$5,631.68	
Nasco - CHS Art Tables	\$7,945.99	\$0.00	100%	\$7,945.99	
Flinn Scientific - MHS Science Equipment	\$44,091.93	\$0.00	100%	\$44,091.93	
Southern NH Univ. - CHS Basketball Facility Rental 5x	\$4,050.00	\$0.00	100%	\$4,050.00	
Williams Communications - Beech Intercom System	\$37,839.00	\$0.00	100%	\$37,839.00	
Williams Communications - Parkside Ceiling Speakers	\$3,235.00	\$3,235.00	0%		
WB Mason - Memorial	\$4,015.10	\$0.00	100%	\$4,015.10	
WB Mason - Central	\$7,543.79	\$0.00	100%	\$7,543.79	
WB Mason - Bakersville	\$14,698.19	\$0.00	100%	\$14,698.19	
WB Mason - Beech	\$11,873.47	\$0.00	100%	\$11,873.47	
WB Mason - Green Acres	\$14,306.41	\$0.00	100%	\$14,306.41	
WB Mason - Gossler	\$3,816.40	\$0.00	100%	\$3,816.40	
WB Mason - Hallsville	\$11,208.76	\$0.00	100%	\$11,208.76	
WB Mason - Highland Goffes Falls	\$15,857.85	\$0.00	100%	\$15,857.85	
WB Mason - Jewett	\$3,104.02	\$0.00	100%	\$3,104.02	
WB Mason - McDonough	\$6,143.76	\$0.00	100%	\$6,143.76	
WB Mason - Northwest	\$2,707.09	\$0.00	100%	\$2,707.09	
WB Mason - Parker-Varney	\$17,030.40	\$0.00	100%	\$17,030.40	
WB Mason - Smyth	\$12,001.60	\$0.00	100%	\$12,001.60	
WB Mason - Webster	\$15,776.14	\$0.00	100%	\$15,776.14	
WB Mason - Weston	\$17,626.68	\$0.00	100%	\$17,626.68	
WB Mason - Wilson	\$6,617.93	\$0.00	100%	\$6,617.93	
Apple Computer - Central 6 eMacs/6 HP All-in-One	\$5,695.10	\$0.00	100%	\$5,695.10	
Statefine Sports - Southside & Parkside Volleyball Stands	\$6,100.00	\$0.00	100%	\$6,100.00	
Doty & Sons - Concrete Receptacles	\$29,499.60	\$0.00	100%	\$29,499.60	
WB Mason - Hillside Storage cabinets/Coat trees	\$3,585.06	\$0.00	100%	\$3,585.06	

3



DESIGN BUILD PROJECT - PAGE 4 OF 5					
AUTHORIZED VENDOR DESCRIPTION AND APPROVAL DATE	BUDGET	AMOUNT ENCUMBERED	PERCENT COMPLETE	AMOUNT EXPENDED	RETAINAGE HELD
(Program FF&E-continued)					
WB Mason - Southside Storage cabinets/Coat rack	\$2,767.85	\$0.00	100%	\$2,767.85	
Famous Lockers - Memorial Football Lockers	\$20,800.00	\$0.00	100%	\$20,800.00	
Highway Dept. - Southside Repave Parking Lot	\$13,521.15	\$0.00	100%	\$13,521.15	
Traffic Dept. - Post Signs & Stripe Parking Lot	\$1,294.41	\$0.00	100%	\$1,294.41	
Highway Dept. - Hillside Excavate Waterline & Pave Portal	\$2,848.32	\$0.00	100%	\$2,848.32	
Penney Fence - Southside Guardrail Relocation	\$1,300.00	\$0.00	100%	\$1,300.00	
DRG Construction - Install white boards in grade schools	\$4,095.00	\$0.00	100%	\$4,095.00	
WB Mason - Memorial 5 Shelves	\$1,225.00	\$0.00	100%	\$1,225.00	
WB Mason-Nurse panels CHS,WHS,MHS,Southside,Hillside	\$375.00	\$0.00	100%	\$375.00	
Home Depot - Southside Portable Restore Site	\$967.17	\$0.00	100%	\$967.17	
Otis Elevator - Decommission CHS-Prac Arts Elevator	\$2,161.00	\$0.00	100%	\$2,161.00	
BK Systems - Restore Fire Alarm Panel after Portable move	\$699.00	\$0.00	100%	\$699.00	
Schiavi - Move Portable to Gossler Park	\$7,630.00	\$0.00	100%	\$7,630.00	
Balance of FF&E		\$8,273.33			
Total FF&E	\$2,000,000.00	\$11,508.33		\$1,988,491.67	
CONTINGENCY					
Contingency/JSBC Approved Expenses	\$5,650,000.00				
Parker-Varney & Highland Open Concept Wall Designs \$155,000	\$0.00				
Mountainside Insulation - McDonough Insulate 27 Cls Rms	\$4,860.00	\$0.00	100%	\$4,860.00	
Memorial - Guardrail Relocation(PennyFence) Pave (Hwy)	\$6,518.47	\$0.00	100%	\$6,518.47	
Memorial - Replace & Install Two New Boilers in CO#26	\$0.00	\$0.00			
Central HS Gymnasium - Painting in CO#21	\$0.00	\$0.00			
Central HS Granite War Memorial	\$27,331.35	\$27,331.35	0%		
Beech Fire Alarm Expansion JSBC 2-21-06	\$115,000.00				
C&M Engineering - Beech Fire Alarm Expansion	\$12,215.00	\$0.00	100%	\$12,215.00	
Union Leader - Beech FA Bid Invitation (2x)	\$359.24	\$0.00	100%	\$359.24	
Spillers Graphics - Beech FA Plans	\$90.36	\$0.00	100%	\$90.36	
G.A. Lafamme - Beech - Fire Alarm Upgrade	\$99,250.00	\$0.00	100%	\$99,250.00	
WW Grainger - Beech FA Upgrade New Fire Door Basement	\$117.00	\$117.00	0%		
Concrete Masonry - Open Concrete for New Fire Door	\$500.00	\$500.00	0%		
Balance of Beech Fire Alarm Expansion Authorization		\$2,468.40			
Foley Buhl Roberts - Hallsville Roof Structure Evaluation	\$29,800.00	\$5,666.58	81%	\$24,133.42	
Pelmac - Central Security System Problems	\$14,124.00	\$0.00	100%	\$14,124.00	
Spillers Graphics - Hallsville Clock Tower Roof Plans	\$6.00	\$0.00	100%	\$6.00	
Chris Tartsa - Hallsville Clock Tower Repairs	\$3,900.00	\$0.00	100%	\$3,900.00	
Gerard A. Lafamme - Hallsville Tower/Move Conduits	\$350.00	\$0.00	100%	\$350.00	
Union Leader - Hallsville Roof Structure Prequal Contractors	\$393.21	\$0.00	100%	\$393.21	
Beech - New metal sign & storefront entrance in CO#26	\$0.00	\$0.00			
Memorial - New Storage Lockers for Band Instruments	\$26,578.00	\$0.00	100%	\$26,578.00	
The Grout Guy - Bakersville - Regrout Hallway Tile	\$8,400.00	\$0.00	100%	\$8,400.00	
Hallsville - UPS Store Mail Bid Packets	\$14.00	\$0.00	100%	\$14.00	
Hallsville - Contractor Repairs - Approved JSBC6/6/06	\$0.00				
Hallsville - Structural/Roof Repairs - Inv. To Bid	\$196.61	\$0.00	100%	\$196.61	
DMJM Program Management - Contract Amendment	\$683,822.00	\$278,138.46	59%	\$405,683.54	
Wiggin & Nourie, P.A. - Manchester PS GP, LLC vs City	\$79,552.14	\$0.00	100%	\$79,552.14	
Memorial - Scraping, Priming, Painting Dust Collection Cyclone	\$940.00	\$940.00	0%		
Central Garage - Payment for Pumps	\$2,500.00	\$2,500.00	0%		
Contingency/ Change Order Number & Amounts					
CO#11: HSMS Unsuitable Soils & EBU Rewiring JSBC	\$32,724.20	\$32,724.20			
CO #12 Hillside/Southside MS Stairs JSBC 11/25/04	\$325,453.00	\$325,453.00			
CO#13: Central Intercom/Webster Acoustical Ceiling	\$16,352.00	\$16,352.00			
CO#14: Hazmat Removal JSBC 3/22/05	\$848,864.12	\$848,864.12			
CO#15 CHS Bleacher/WHS Locker/Southside Bleacher	\$346,519.82	\$346,519.82			
CO#16 CHS & Parkside Changes & Weston Painting	\$44,466.00	\$44,466.00			
CO#17 CHS, WHS, McDonough, Bakerville, HGF, Pk-Varn	\$102,150.00	\$102,150.00			
CO#18 MHS, Beech and West Various Changes	\$7,865.00	\$7,865.00			
CO#19 MHS, WHS, Hillside, Southside, Hallsville, NW, MST	\$97,236.48	\$97,236.48			
CO#20 MHS, CHS, Hillside, Southside, Beech	\$93,005.00	\$93,005.00			



Manchester Public
School Facilities
Improvement Project

DMJM
AN ARCADIAN COMPANY
Project Office

222 South Jewett Street · Manchester, NH 03103
T 603.644.0410 · F 603.644.0411

DESIGN BUILD PROJECT - PAGE 5 OF 5					
AUTHORIZED VENDOR DESCRIPTION AND APPROVAL DATE	BUDGET	AMOUNT ENCUMBERED	PERCENT COMPLETE	AMOUNT EXPENDED	RETAINAGE HELD
Contingency/ Change Order Number & Amounts-Continued					
CO#21 MHS, CHS, WHS, Hillside, McDonough, Hallsville, MST	\$78,581.94	\$78,581.94			
CO#22 CHS, WHS, Hillside, Southside, Parkside, Beech, Weston	\$5,745.00	\$5,745.00			
CO#23 Beech Bleachers & Stair Treads, Bakesville Chimney Reduction	\$14,297.00	\$14,297.00			
CO#24 Central, Hallsville and CR for Parkside	\$16,113.00	\$16,113.00			
CO#25 Memorial, Central, Southside, Highland and Cr for Hillside	\$128,992.77	\$128,992.77			
CO#26 CHS, MHS, WHS, Southside, McDonough, and Beech	\$403,493.16	\$403,493.16			
Balance for Future Contingency Allocations		\$2,083,855.73			
<i>Contingency Authorized to Date</i>	\$3,566,144.27	\$4,963,376.01		\$686,623.99	
JSBC APPROVED CONTINGENCY BALANCE	\$2,083,855.73				
UNENCUMBERED PROJECT FUNDS	(\$85,252.52)				
ENCUMBERED/EXPENDED TOTAL	\$109,332,971.52	\$7,798,813.41		\$101,534,158.11	
TOTAL	\$109,247,719.00				

3

TO: Joint Building Committee
FROM: Building & Sites Committee
DATE: February, 2007
RE: FY08 CIP—Facilities

At the Building & Sites Committee meeting held on January 22, 2006, the Committee reviewed recommendations relative to the above-referenced. After due and careful consideration the Committee recommends:

To see if the cost for the roof structure repairs at Hallsville School could come from the contingency fund of the design/build project.


The motion passed by unanimous vote.


Respectfully submitted,
Arthur Beaudry, Chairman
Bob Leonard
Dave Gelinis
Russ Ouellette
*Chris Herbert

**Katherine Labanaris

*Member Absent
**Non-member attending

IN BOARD OF SCHOOL COMMITTEE
Adopted.....2007


Suzanne O. Sears Board Clerk



4
