ADDENDUM NO. 1
May 14, 2012
DRILLING AND BLASTING ROCK
SKYLINE DRIVE SEWER PROJECT
Bid No. FY12-500-87
City of Manchester
Department of Highways

The attention of all bidders submitting proposals for the above project is called to the following changes to the Contract Documents. The items set forth herein, whether or clarification, omission, addition or substitution are to be included in and shall form a part of the proposal submitted.

Bidders shall acknowledge receipt of this Addendum by writing "Addendum No. 1 Received" on page 12 of the Proposal.

ADDENDUM NO. 1:

Purpose of Addendum:

To add or change the following:

- The successful bidder will be required to begin the project immediately upon award of the contract and notice to proceed and match his schedule with the City's.
- The successful bidder will be required to expedite the pre-blast survey, completing each street individually instead of all three as a whole. The intent is to complete portions of the pre-blast survey to allow construction to begin as early as possible.
- The contractor will be required to provide adequate crews (no more than two) to match the City's schedule.

END OF ADDENDUM

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
1		Dunbarton Road - Cleanup	3 days	Mon 5/7/12	Wed 5/9/12	
2		Dunbarton Road - Overlay	2 days	Thu 5/10/12	Fri 5/11/12	
3		DW Highway Drain				
4		Drain Crew	12 days	Tue 5/8/12	Wed 5/23/12	
5						
6		Greeley Street Drain				
7		Drain Crew	12 days	Tue 5/29/12	Wed 6/13/12	4
8						
9		Crack Sealing				
10		Blasting Contract Bid Opening	1 day	Thu 5/17/12	Thu 5/17/12	
11		Blasting Contract Award/Signing	1 day	Wed 5/23/12	Wed 5/23/12	
12		Blasting Contract Preblast Survey	10 days	Thu 5/24/12	Thu 6/7/12	
13						
14						
15						
16						
17		Skyline Proj. - Bernice Ave.				
18		Main Drain Crew (Up to MH J)	3 days	Thu 6/7/12	Mon 6/11/12	
19		Main Drain Crew (Up to MH K)	3 days	Wed 6/13/12	Fri 6/15/12	
20		Main Drain Crew (Up to MH L)	4 days	Mon 6/18/12	Thu 6/21/12	19
21		Main Drain Crew (Up to MH M)	3 days	Fri 6/22/12	Tue 6/26/12	20
22		Main Drain Crew (Up to MH N)	2 days	Wed 6/27/12	Thu 6/28/12	21
23						
24		Blasting Contract (Bernice to MH K)	2 days	Mon 6/11/12	Tue 6/12/12	17
25		Blasting Contract (Bernice to MH L)	4 days	Wed 6/13/12	Mon 6/18/12	24
26		Blasting Contract (Bernice to MH M)	2 days	Wed 6/20/12	Thu 6/21/12	25
27		Blasting Contract (Bernice to MH M)	2 days	Fri 6/22/12	Mon 6/25/12	26
28						
29		2nd Drain Crew (Service to #33)	1 day	Mon 6/18/12	Mon 6/18/12	
30		2nd Drain Crew (Service to #30)	1 day	Tue 6/19/12	Tue 6/19/12	29
31		2nd Drain Crew (Service to #50)	1 day	Wed 6/20/12	Wed 6/20/12	30
32		2nd Drain Crew (Service to #55)	2 days	Thu 6/21/12	Fri 6/22/12	31
33		2nd Drain Crew (Service to#77)	2 days	Mon 6/25/12	Tue 6/26/12	32
34		2nd Drain Crew (Service to Lot 6)	2 days	Wed 6/27/12	Thu 6/28/12	33
35		2nd Drain Crew (Service to #151)	2 days	Fri 6/29/12	Mon 7/2/12	34
36		2nd Drain Crew (Service to #183)	2 days	Tue 7/3/12	Thu 7/5/12	35
37						
38		Blasting Contract (Meadow Glento Serv. To #55)	2 days	Thu 6/21/12	Fri 6/22/12	
39		Blasting Contract (Meadow Glento Serv. to #77)	2 days	Mon 6/25/12	Tue 6/26/12	38
40		Blasting Contract (Meadow Glento Serv. to #Lot 6)	2 days	Wed 6/27/12	Thu 6/28/12	39
41		Blasting Contract (Meadow Glento Serv. to #151)	2 days	Fri 6/29/12	Mon 7/2/12	40
42		Blasting Contract (Meadow Glento Serv. to #183)	2 days	Tue 7/3/12	Thu 7/5/12	41
43						
44		Skyline Proj. - Meadow Glen Dr.				
45		Main Drain Crew (Up to MH E)	3 days	Fri 6/29/12	Tue 7/3/12	22
46		Main Drain Crew (Up to MH F)	5 days	Thu 7/5/12	Wed 7/11/12	45
47		Main Drain Crew (Up to MH G)	4 days	Thu 7/12/12	Tue 7/17/12	46
48		Main Drain Crew (Up to MH H)	3 days	Wed 7/18/12	Fri 7/20/12	47
49		Main Drain Crew (Up to MH I)	3 days	Mon 7/23/12	Wed 7/25/12	48
50						
51		Blasting Contract (Meadow Glen to MH F)	2 days	Mon 7/2/12	Tue 7/3/12	
52		Blasting Contract (Meadow Glento MH G)	5 days	Thu 7/5/12	Wed 7/11/12	51
53		Blasting Contract (Meadow Glen to MH H)	2 days	Thu 7/12/12	Fri 7/13/12	52
54						
55		2nd Drain Crew (Service to #131)	1 day	Thu 7/5/12	Thu 7/5/12	
56		2nd Drain Crew (Service to #33)	1 day	Fri 7/6/12	Fri 7/6/12	55
57		2nd Drain Crew (Service to #30)	1 day	Tue 7/10/12	Tue 7/10/12	56FS+1 day
58		2nd Drain Crew (Service to #55)	1 day	Wed 7/11/12	Wed 7/11/12	57
59		2nd Drain Crew (Service to #50)	1 day	Fri 7/13/12	Fri 7/13/12	58FS+1 day
60		2nd Drain Crew (Service to#67)	2 days	Wed 7/18/12	Thu 7/19/12	59FS+2 days
61		2nd Drain Crew (Service to #70)	2 days	Fri 7/20/12	Mon 7/23/12	60
62		2nd Drain Crew (Service to #117)	2 days	Tue 7/24/12	Wed 7/25/12	61
63		2nd Drain Crew (Service to #101)	2 days	Thu 7/26/12	Fri 7/27/12	62
64		2nd Drain Crew (Service to #135)	2 days	Mon 7/30/12	Tue 7/31/12	63
65						
66		Blasting Contract (Meadow Glen to Serv. To #67)	2 days	Wed 7/18/12	Thu 7/19/12	
67		Blasting Contract (Meadow Glento Serv. to #70)	2 days	Fri 7/20/12	Mon 7/23/12	66
68		Blasting Contract (Meadow Glento Serv. to #117)	2 days	Tue 7/24/12	Wed 7/25/12	67
69		Blasting Contract (Meadow Glento Serv. to #101)	2 days	Thu 7/26/12	Fri 7/27/12	68
70		Blasting Contract (Meadow Glento Serv. to #135)	2 days	Mon 7/30/12	Tue 7/31/12	69
71						
72		Skyline Proj. - Skyline Dr.				
73		Main Drain Crew (Up to MH A)	4 days	Thu 7/26/12	Tue 7/31/12	49
74		Main Drain Crew (Up to MH B)	4 days	Wed 8/1/12	Mon 8/6/12	73
75		Main Drain Crew (Up to MH C)	6 days	Tue 8/7/12	Tue 8/14/12	74
76		Main Drain Crew (Up to MH D)	2 days	Wed 8/15/12	Thu 8/16/12	75
77						
78		Blasting Contract (Skyline to MH B)	2 days	Mon 7/30/12	Tue 7/31/12	
79		Blasting Contract (Skyline to MH C)	4 days	Wed 8/1/12	Mon 8/6/12	78
80		Blasting Contract (Skyline to MH D)	2 days	Tue 8/7/12	Wed 8/8/12	79
81						
82		2nd Drain Crew (Service to #30)	1 day	Tue 8/7/12	Tue 8/7/12	
83		2nd Drain Crew (Service to #33)	1 day	Wed 8/8/12	Wed 8/8/12	82
84		2nd Drain Crew (Service to #40)	2 days	Mon 8/13/12	Tue 8/14/12	83
85		2nd Drain Crew (Service to #41)	2 days	Wed 8/15/12	Thu 8/16/12	84
86		2nd Drain Crew (Service to #57)	2 days	Fri 8/17/12	Mon 8/20/12	85
87		2nd Drain Crew (Service to #60)	2 days	Tue 8/21/12	Wed 8/22/12	86
88		2nd Drain Crew (Service to Lot 12)	2 days	Thu 8/23/12	Fri 8/24/12	87
89		2nd Drain Crew (Service to Lot 11)	2 days	Mon 8/27/12	Tue 8/28/12	88
90						
91		Blasting Contract (Skyline to Service to #40)	2 days	Mon 8/13/12	Tue 8/14/12	
92		Blasting Contract (Skyline to Service to #41)	2 days	Wed 8/15/12	Thu 8/16/12	91
93		Blasting Contract (Skyline to Service to #57)	2 days	Fri 8/17/12	Mon 8/20/12	92
94		Blasting Contract (Skyline to Service to #60)	2 days	Tue 8/21/12	Wed 8/22/12	93
95		Blasting Contract (Skyline to Service to Lot 12)	2 days	Thu 8/23/12	Fri 8/24/12	94
96		Blasting Contract (Skyline to Serv. To Lot 11?)	2 days	Mon 8/27/12	Tue 8/28/12	95
97						
98		Reclaim/Rebuild Roadways	6 days	Wed 8/29/12	Thu 9/6/12	
99		Install Binder Layer	2 days	Fri 9/7/12	Mon 9/10/12	98
100		Install Curb	40 days	Tue 9/11/12	Wed 11/7/12	99
101		Clean-up Activities	5 days	Thu 11/8/12	Thu 11/15/12	100
102		Final Overlay	2 days	Fri 11/16/12	Mon 11/19/12	101
103						
104						
105		<New Task>				
106		<New Task>				
107		<New Task>				
108		<New Task>				
109		<New Task>				
110		<New Task>				
111		<New Task>				
112		<New Task>				
113		<New Task>				
114		<New Task>				
115		<New Task>				
116		<New Task>				
117		<New Task>				
118		<New Task>				
119		<New Task>				
120		<New Task>				
121		<New Task>				
122		<New Task>				
123		<New Task>				
124		<New Task>				

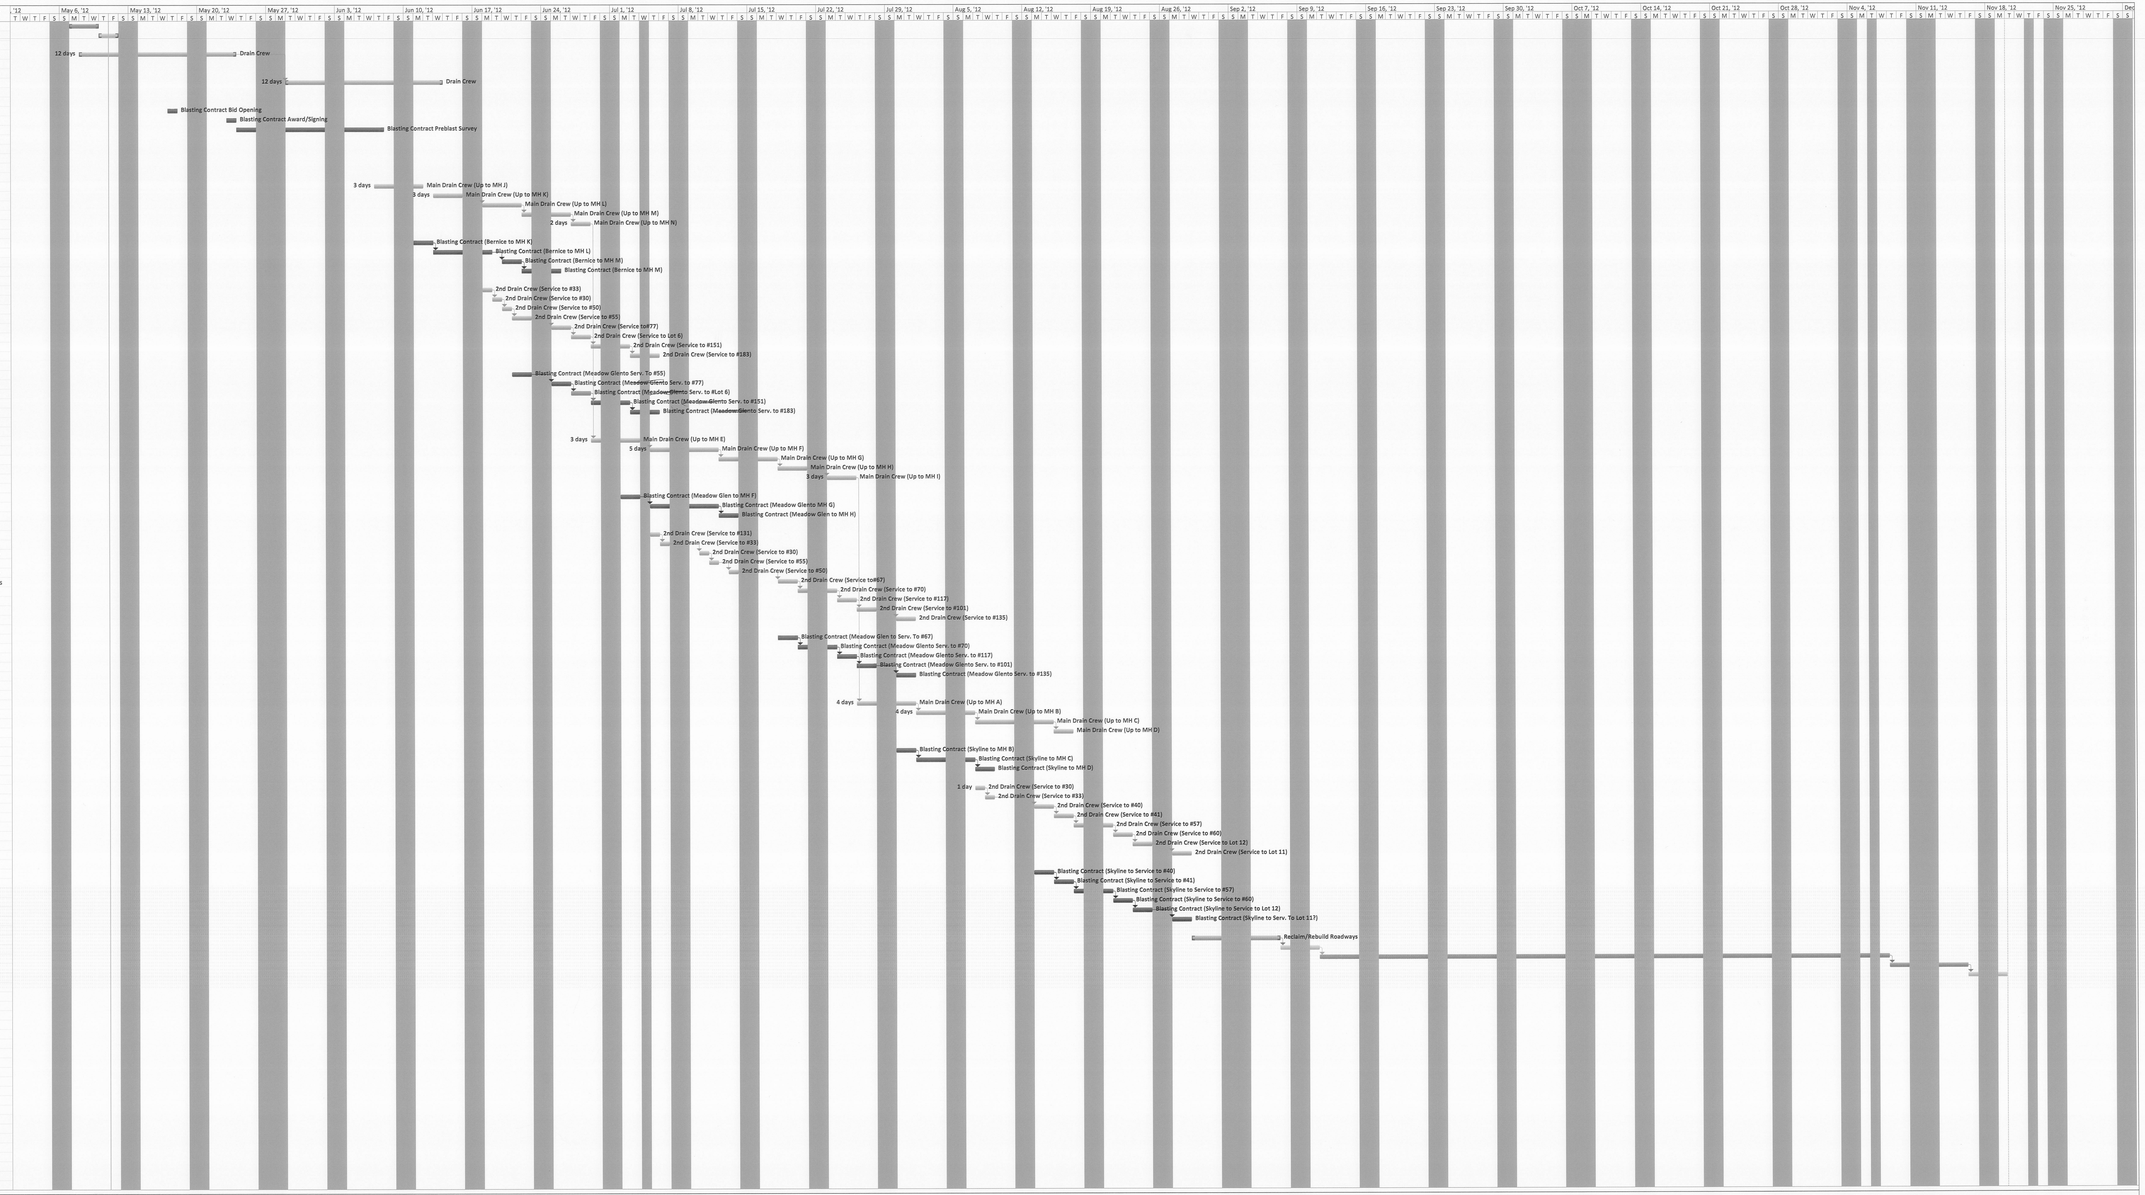

Project: Schedule of Construction
Date: Fri 5/11/12

Task | Split | Milestone | Summary | Project Summary | External Tasks | External Milestone | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | Deadline | Progress
